

WEEKLY UPDATE WITH PHOTOS For week commencing 6th May 2024

- Core B External brickwork is complete and Core A brickwork is nearing completion.
- The communal walls have been closed on the First, Second, Third, Fourth floors with the Fifth floor in progress.
- Tape and Jointing has now completed on the Eighth floor with Ground floor in progress.
- The plant room works are in progress.
- The external insulation is complete to the Seventh floor.
- Electrical second fix has progressed up to the Seventh and Eighth floor.
- Solar panels are now in position on the Sixth & Ninth floor roof.
- The air source heat pumps are installed on the Ninth-floor roof.
- Internal doors and frames are now fitted to the Seventh floor with Eighth in progress.
- Kitchen installation is complete to the Seventh floor with Eighth due to progress next week.
- Core B lift installation is complete with core A nearing completion.
- Tiling to kitchens and bathrooms are complete to the First, Second and Third floors with the Fourth Floor progressing well.
- The site will be open on Saturday 04/05/2024.



Tony Johnson
Senior Site Manager

Contact our Social Value and Community Team

☎ 0800 032 6760 (free phone) 8am to 8pm, seven days a week

✉ residents@hill.co.uk

✍ The Powder House
Gunpowder Mill
Powdermill Lane
Waltham Abbey
Essex, EN9 1BN



Thamesview House Bulletin

6th May 2024




Benchmark Plot Second Coat



ASHP Enclosure



Benchmark Plot External Mastic

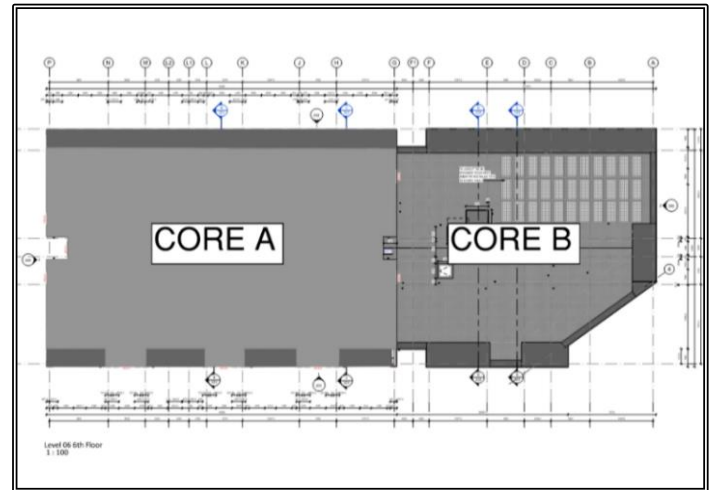

Core Identification



Tony Johnson
Senior Site Manager

Contact our Social Value and Community Team

☎ 0800 032 6760 (free phone) 8am to 8pm, seven days a week

✉ residents@hill.co.uk

✍ The Powder House
Gunpowder Mill
Powdermill Lane
Waltham Abbey
Essex, EN9 1BN

